



# Extension , Renovation and Modernisation of Irrigation Infrastructure Cauvery Sub Basin



## Physical Progress

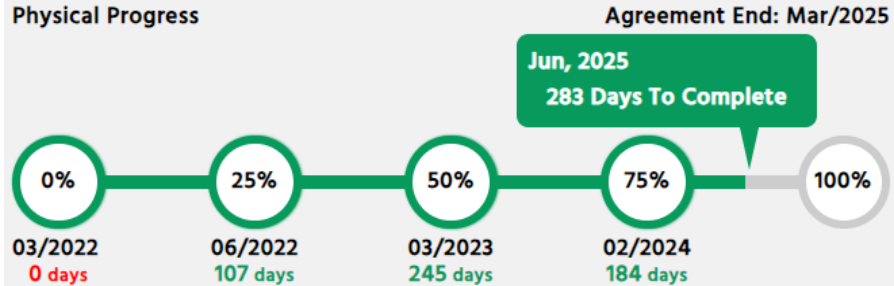

## Financial Progress



Announcement Year

2019 - 2020

Admin Sanction

28.12.2020

1361 Days

Work Order Issued

02.02.2021

Estimated Cost

3,607.3 Cr

Work Progress (%)

87 % ↑

+ 4 %

Financial Progress

77 % ↑

+ 2 %

Previous End Date

31.03.2025

Revised End Date

30.06.2025

Issue /Status

Out of 33 packages ,12 packages completed and 88% of work completed in 21 packages

- Administrative Sanction accorded for Rs. 224.80crore in G.O(Ms) No.331 Public Works (W1) Dept., dated 28.12.2020 for 2 packages.
- Administrative Sanction accorded for Rs.3159.20crore in G.O(Ms) No.40 Public Works (W1) Dept., dated 08.02.2021 for 31 packages.
- Revised Administrative Sanction accorded for Rs.3607.30 crore in G.O. (Ms) No.13 WR.,(S2) Dept., dated 06.02.2024.
- **Components:**Regulators-275 , Head sluices-1205, Bed dam -16, inlet & outlet-468, Syphon-103, Aqueducts-13, Retaining wall, River training wall & RCC wall -39.49 km, regrading of channel -87.10 km
- About 3,54,147 acre of ayacut in Thanjavur, Nagapattinam, Pudukkottai, Mayiladuthurai and Tiruvarur Districts would be benefited.
- Work commenced on 04.03.2022 and 88 % work completed. Proposed to complete the work on 30.06.2025
- Expenditure incurred: Rs.2,932.07 crore



**Before Execution**

**Grade Wall at Cauvery River @ Mile 35/06+50 in Kaduveli Village of Thiruvaiyar Taluk in Thanjavur District**



**After Execution**



**Before Execution**

•Regulator across Nattar river at LS 60/6+50 Srinivasanallur Village of Kumbakonam Taluk in Thanjavur District.



**After Execution**
