


KARUR DISTRICT

Kudimaramath works for the year	2020-21 , G.O (Ms) No.98, Public Works (W1) Department, Dated:- 22.04.2020.		
Sl.No	01		
Name of work	Construction of flood protection wall in weak portion at LS 24800 m to 25200 m , removal of bushes and desilting in branches of Right bank canal off taking at LS 197.20 km in Amaravathi River of Manmangalam Taluk in Karur District"		
Estimate Amount (Rs. In lakhs)	35.00	Date of commencement	21.08.2020
Expenditure w.r.t 90% of Estimate Amount (Rs. In lakhs)	29.43	Date of completion (If the work is in progress, mention the probable date of completion)	13.10.2020
Nature of work	Light Jungle Clearance & Construction of Flood Protection Wall	Progress of work (% Completed)	100%
Name of the Farmers Association by which work has been executed	Mayanur pasana vivasayical nala sangam.		

PHOTOS

The photos before execution and after execution should be in the same location & orientation.

Before Execution

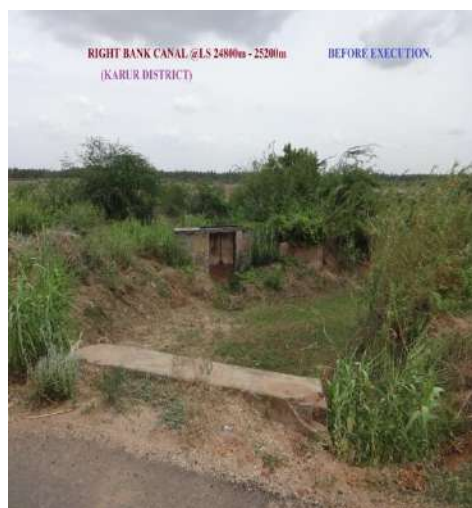

After Execution



Kudimaramath works for the year	2020-21 , G.O (Ms) No.98, Public Works (W1) Department, Dated:- 22.04.2020.		
Sl.No	02		
Name of work	Construction of flood protection wall in weak portion at LS 35010 m to 36000 m , clearing the bushes and desilting in branch of Left bank canal off taking at LS 181.44 km in Amaravathi River of Aravakkuruchi Taluk in Karur District."		
Estimate Amount (Rs. In lakhs)	30.00	Date of commencement	15.07.2020
Expenditure w.r.t 90% of Estimate Amount (Rs. In lakhs)	26.00	Date of completion (If the work is in progress, mention the probable date of completion)	25.02.2020
Nature of work	Construction of Flood Protection Wall	Progress of work (% Completed)	100%
Name of the Farmers Association by which work has been executed	Kelakkupaguthi Rajavaikkal pasana vevasaikal Nalasangam, Panchamadevi, Karur.		

PHOTOS

The photos before execution and after execution should be in the same location & orientation.

Before Execution



After Execution



Kudimaramath works for the year	2020-21 , G.O (Ms) No.98, Public Works (W1) Department, Dated:- 22.04.2020.		
Sl.No	03		
Name of work	Construction of flood protection wall in weak portion at LS 20200 m to 20600 m and 23630m to 23670m and clearing the bushes in Left bank canal off taking at LS 181.44 km in Amaravathi River of Aravakurichi Taluk in Karur District."		
Estimate Amount (Rs. In lakhs)	43.50	Date of commencement	22.06.2020
Expenditure w.r.t 90% of Estimate Amount (Rs. In lakhs)	24.09192	Date of completion (If the work is in progress, mention the probable date of completion)	03.09.2020
Nature of work	Clearing the light jungle & Construction of Flood Protection Wall.	Progress of work (% Completed)	100%
Name of the Farmers Association by which work has been executed	Pallapalayam Raja vaikkal Neerinai Payanpaduthum Vevasaikkal Nalasankam, Karur.		

PHOTOS

The photos before execution and after execution should be in the same location & orientation.

Before Execution



After Execution



Kudimaramath works for the year	2020-21		
Sl.No	04		
Name of work	Rehabilitation of Left Low Level Canal and Left High Level Canal of Nanganjiyar Reservoir Project under the Jurisdiction of Nanganjiyar Main canal senthamangalam West village Water User Association in senthamangalam West Village of Aravakurichi Taluk in Karur District		
Estimate Amount (Rs. In lakhs)	9.00	Date of commencement	23.06.2020
Expenditure w.r.t 90% of Estimate Amount (Rs. In lakhs)	7.53	Date of completion (If the work is in progress, mention the probable date of completion)	28.10.2020
Nature of work	Retaining wall, Inlet and Bund Strengthening	Progress of work (% Completed)	100%
Name of the Farmers Association by which work has been executed	Nanganjiyar Main canal senthamangalam West Water User Association		

JUNGLE CLEARANCE WORK

BEFORE EXECUTION



AFTER EXECUTION



INLET WORK

BEFORE EXECUTION



AFTER EXECUTION



JEEP TRACK STRENGTHENING

BEFORE EXECUTION



AFTER EXECUTION



BEFORE EXECUTION



AFTER EXECUTION



PROTECTION WALL WORK

BEFORE EXECUTION



AFTER EXECUTION



DEMARCATON STONE

BEFORE EXECUTION



DURING EXECUTION



Kudimaramath works for the year	2020-21 , G.O (Ms) No.98, Public Works (W1) Department, Dated:- 22.04.2020.		
Sl.No	05		
Name of work	Renovation of Head sluice portion, repairs to leading channel, common bank of chettipalayam anicut and clearing the bushes of Right bank canal off taking at LS 197.20 km in Amaravathi River of Manmangalam Taluk in Karur District."		
Estimate Amount (Rs. In lakhs)	54.00	Date of commencement	23.07.2020
Expenditure w.r.t 90% of Estimate Amount (Rs. In lakhs)	9.68	Date of completion (If the work is in progress, mention the probable date of completion)	17.08.2020.
Nature of work	Clearing the light jungle, Renovation of head sluices & Repairs to leading channel.	Progress of work (% Completed)	100%
Name of the Farmers Association by which work has been executed	Thirumanilaiyur vaikkal Pasana vevasaikal Nalasangam. Sellandipalayam, Karur.		

PHOTOS

The photos before execution and after execution should be in the same location & orientation.

Before Execution



After Execution



Kudimaramath works for the year	2020-21 , G.O (Ms) No.98, Public Works (W1) Department, Dated:- 22.04.2020.		
Sl.No	06		
Name of work	Construction flood protection wall in weak portion in LS 3500 m and LS 19900 m and removal of bushes from LS 0/0 to 4000 m in Chinnadharapuram channel off taking at LS 148.32 km in Amaravathi River of Aravakkuruchi Taluk in Karur District."		
Estimate Amount (Rs. In lakhs)	25.00	Date of commencement	29.06.2020
Expenditure w.r.t 90% of Estimate Amount (Rs. In lakhs)	22.30	Date of completion (If the work is in progress, mention the probable date of completion)	06.10.2020
Nature of work	Clearing the light jungle, R.R masonry & Earth work for foundation.	Progress of work (% Completed)	100%
Name of the Farmers Association by which work has been executed	Sirutharai Vaikkal Pasana Vivasayikal Nala Sangam		

PHOTOS

The photos before execution and after execution should be in the same location & orientation.

Before Execution



After Execution



Kudimaramath works for the year	2020-21		
SI.No	07		
Name of work	Rehabilitation of Right Low Level Canal and Right High Level Canal of Nanganjiyar Reservoir Project under the Jurisdiction of Nanganjiyar Main canal senthamangalam East village Water User Association in senthamangalam East Village of Aravakurichi Taluk in Karur District		
Estimate Amount (Rs. In lakhs)	7.00	Date of commencement	23.06.2020
Expenditure w.r.t 90% of Estimate Amount (Rs. In lakhs)	6.00	Date of completion (If the work is in progress, mention the probable date of completion)	6.11.2020
Nature of work	Retaining wall, Inlet and Bund Strengthening	Progress of work (% Completed)	100%
Name of the Farmers Association by which work has been executed	Nanganjiyar Main canal senthamangalam East Water User Association		

PROTECTION WALL WORK

BEFORE EXECUTION



AFTER EXECUTION



INLET WORK

BEFORE EXECUTION



AFTER EXECUTION



JUNGLE CLEARANCE WORK

BEFORE EXECUTION



AFTER EXECUTION



PROTECTION WALL WORK

BEFORE EXECUTION



AFTER EXECUTION



BEFORE EXECUTION



AFTER EXECUTION



DEMARICATION STONE

Kudimaramath works for the year	2020-21 , G.O (Ms) No.98, Public Works (W1) Department, Dated:- 22.04.2020.		
Sl.No	08		
Name of work	Construction of protection wall in weak portion between LS 7500 m to 8500 m and removal of bushes from LS 6000 m to 8000 m in Nanjaikalkurichi channel off taking at LS 171.20 km in Amaravathi River of Aravakkuruchi Taluk in Karur District ".		
Estimate Amount (Rs. In lakhs)	10.00	Date of commencement	18.06.2020
Expenditure w.r.t 90% of Estimate Amount (Rs. In lakhs)	8.90	Date of completion (If the work is in progress, mention the probable date of completion)	31.08.2020
Nature of work	Clearing light jungle Construction of Flood Protection Wall.	Progress of work (% Completed)	100%
Name of the Farmers Association by which work has been executed	Nanjaikalkurichi vaikkal neerinai payanpaduthum vivasayikal nala sangam.		

PHOTOS

The photos before execution and after execution should be in the same location & orientation.

Before Execution



After Execution

