


# Centrally Sponsored Schemes

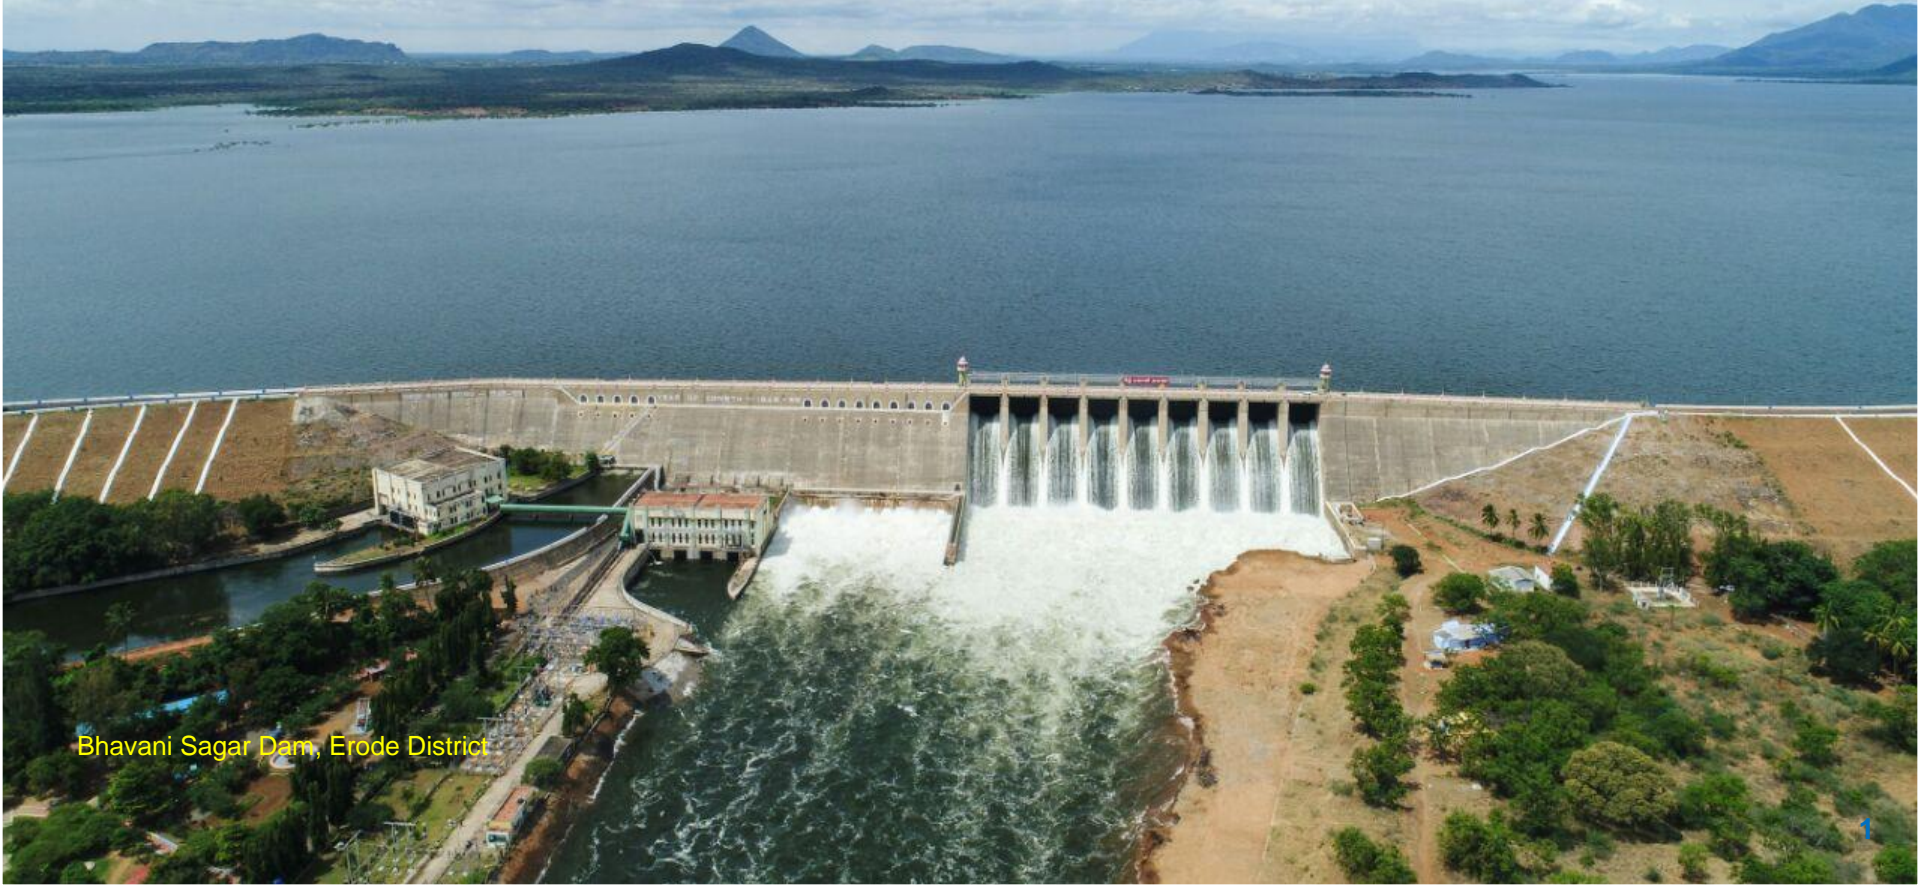

Bhavani Sagar Dam, Erode District

# Repair, Renovation and Restoration (RRR) of water bodies

- Repair, Renovation and Restoration (RRR) is a Centre-State shared scheme under PMKSY.
- This scheme involves the following components:
  - Standardisation of tank bund to standards.
  - De-silting the tank bed to restore the storage capacity
  - Reconstruction / Improvements to sluices and surplus arrangements
  - De-silting and strengthening of feeder channel to ensure supply to tanks

# Repair, Renovation & Restoration (RRR) of Water bodies



(Rs. in crore)

| Phase      | No. of works | Completed | In progress | To be taken up | Est. Amt. | Expr. | State share | Government of India |          |                |
|------------|--------------|-----------|-------------|----------------|-----------|-------|-------------|---------------------|----------|----------------|
|            |              |           |             |                |           |       |             | Share               | Released | To be released |
| I,II & III | 153          | 153       |             |                | 77.75     | 73.26 | 25.00       | 48.26               | 18.21    | 30.06          |
| IV & V     | 92           | 92        |             |                | 51.04     | 47.39 | 20.27       | 30.31               | 27.48    | 2.83           |

(Rs. in crore)



| Phase        | No. of works | Completed  | In progress | To be taken up | Est. Amt.     | Expr.         | State share   | Government of India |               |                |
|--------------|--------------|------------|-------------|----------------|---------------|---------------|---------------|---------------------|---------------|----------------|
|              |              |            |             |                |               |               |               | Share               | Released      | To be released |
| VI           | 115          | 95         | 20          |                | 75.00         | 41.40         | 31.87         | 43.13               | 24.94         | 18.19          |
| VII          | 85           | 54         | 31          |                | 90.08         | 49.75         | 41.58         | 48.50               | 30.08         | 18.42          |
| VIII         | 100          | 59         | 41          |                | 92.83         | 46.84         | 42.57         | 50.26               | 28.26         | 21.99          |
| IX           | 100          | 1          | 99          |                | 111.48        |               | 50.93         | 60.56               |               | 60.56          |
| X            | 123          |            |             | 123            | 100.07        |               | 40.03         | 60.04               |               | 60.04          |
| <b>TOTAL</b> | <b>768</b>   | <b>454</b> | <b>191</b>  | <b>123</b>     | <b>598.25</b> | <b>258.64</b> | <b>252.25</b> | <b>341.06</b>       | <b>128.97</b> | <b>212.09</b>  |

## Physical Progress

### Chennai Region

| Phase        | No. of works | No. of works Completed | No. of works in progress |
|--------------|--------------|------------------------|--------------------------|
| VI           | 38           | 33                     | 5                        |
| VII          | 26           | 19                     | 7                        |
| VIII         | 26           | 17                     | 9                        |
| IX           | 11           | 0                      | 11                       |
| <b>Total</b> | <b>101</b>   | <b>69</b>              | <b>32</b>                |

### Trichy Region

| Phase        | No. of works | No. of works completed | No. of works in progress |
|--------------|--------------|------------------------|--------------------------|
| VI           | 32           | 18                     | 14                       |
| VII          | 25           | 10                     | 15                       |
| VIII         | 30           | 8                      | 22                       |
| <b>Total</b> | <b>87</b>    | <b>36</b>              | <b>51</b>                |

### Madurai Region

| Phase        | No. of works | No. of works Completed | No. of works in progress |
|--------------|--------------|------------------------|--------------------------|
| VI           | 45           | 44                     | 1                        |
| VII          | 34           | 25                     | 9                        |
| VIII         | 44           | 34                     | 10                       |
| IX           | 89           | 1                      | 88                       |
| <b>Total</b> | <b>212</b>   | <b>104</b>             | <b>108</b>               |



## Tank bund Strengthening



Before Execution



After Execution

Phase IV-Elagiri Tank in Nallampalli Block of Dharmapuri Taluk in Dharmapuri District

## Sluice Reconstruction



Before Execution



After Execution

Phase VIII - Agarakulam in Kalangudi Village of Alangudi Taluk in Pudukkottai District



## Desilting of Surplus Course



Before Execution



After Execution

Phase VII - Illupaikulam Big and Small Tank in Illupaikulam Village of Kariapatti Taluk in Virudhunagar District
