

5. Reclaiming Kazhuveli tank for storage of fresh water and sea water intrusion control measures and recharge shaft Well/ Shafts in Marakanam Block of Villupuram District



Kazhuveli Tail End Regulator

AS	G.O (3D) No.12 PWD (T1) Dept, dated.24.02.2020, Rs. 161.00 cr
RAS	G.O (Ms) No.40 WR(S1) Dept, dated.11.03.2024, Rs. 166.75 cr


Announcement Year	2019-2020
Admin Sanction	2020
Work Order Issued	24.02.2021
Est. Cost (Rs. in cr)	Rs. 166.75 cr
Work Progress(%)	37%
Financial Progress (%)	37%
Commenced on	24.02.2021
Prob. Date of Completion	31.03.2025
Ayacut Benefited in Ha.	----

- The Project is located in Kanthadu village of Marakkanam Taluk in Villupuram District.
- The length of the structure is 196.00 m with storage capacity of 6.6TMC water having a water spread area of 5700 ha.
- It consists of 18 vents of size 9.00 x 1.75 m with the discharging capacity of 30,000 cusecs.
- Work commenced on 24.02.2021 and about 37% of works has been completed with an expenditure of 52.69 crore.

Issues:

- The Water Spread has been announced as Birds Sanctuary. Online application under scrutiny to obtain Forest and Wildlife Clearance.

NAME OF WORK :
RECLAIMING KAZHUVELI TANK FOR STORAGE OF
FRESH WATER AND SEA WATER INTRUSION
CONTROL MEASURES AND RECHARGE SHAFT WELLS / SHAFT
IN MARAKKANAM BLOCK OF VILLUPURAM DISTRICT.

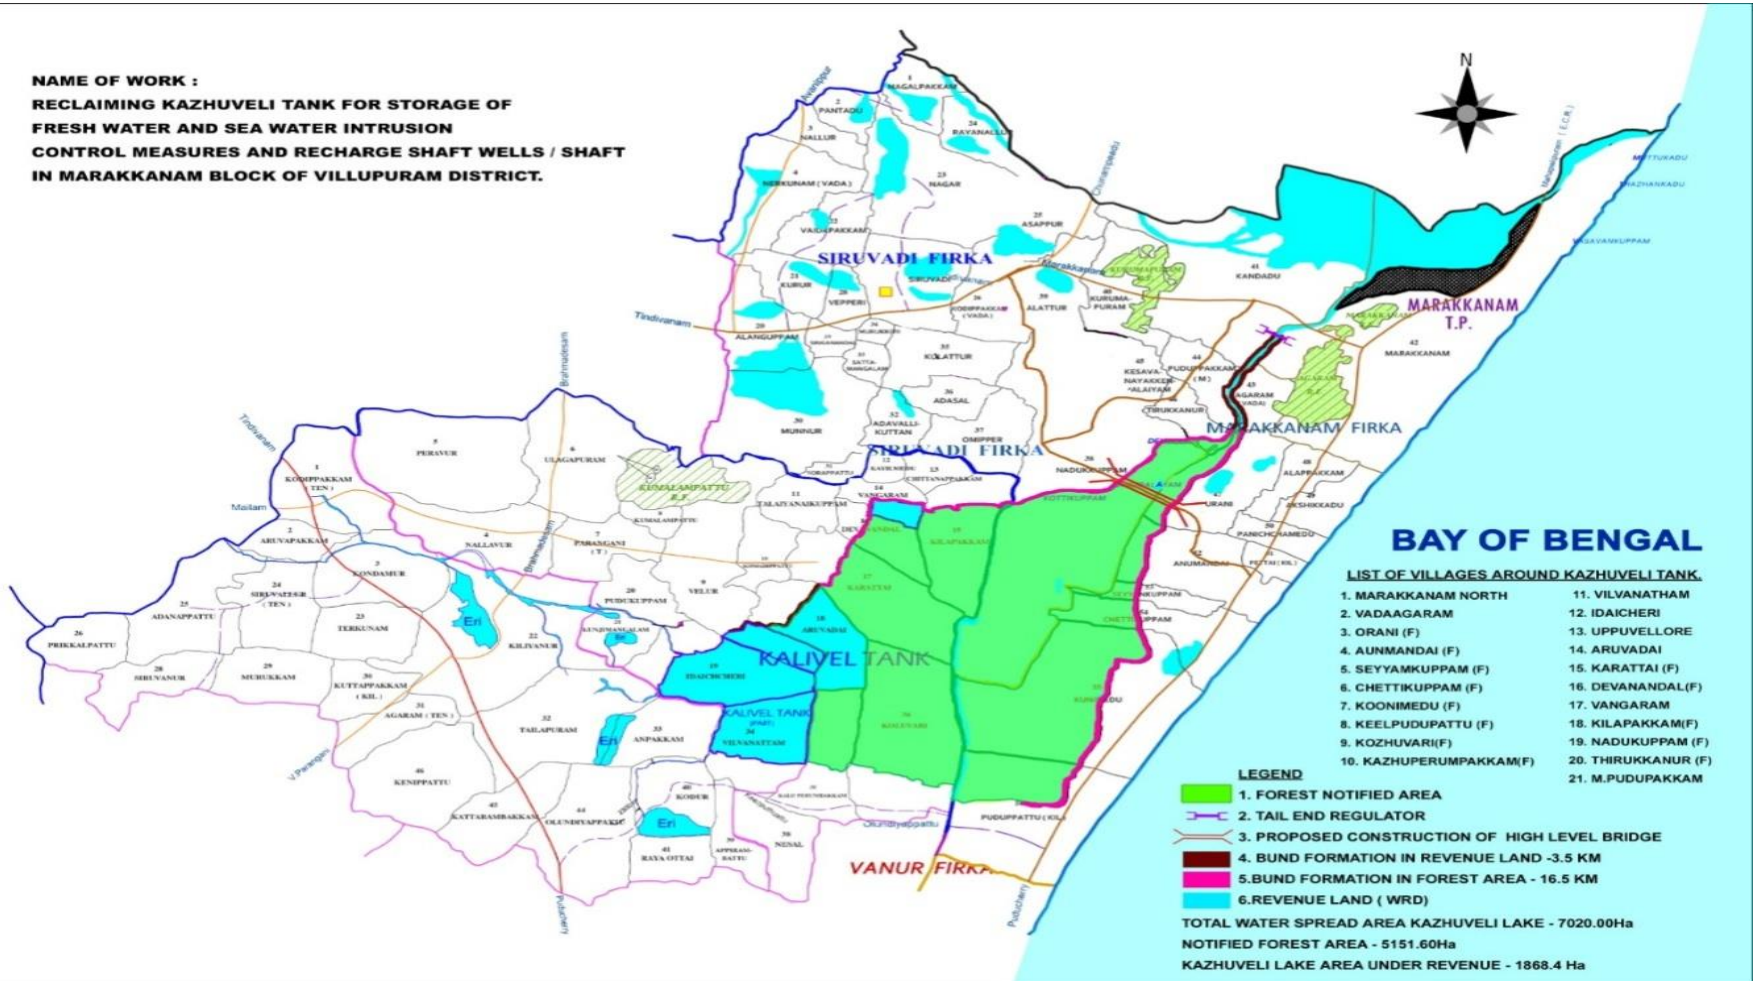



Kazhuveli Tail End Regulator



Kazhuveli Tail End Regulator



Kazhuveli Tank Water Spread Area at LS 12 Km



Kazhuveli Tank Water Spread Area at LS 16 Km
